


Complete Well Summary Sample 11 - Full Data


Deviated - Original Hole, 2009-09-15 10:35:29 AM
Vertical schematic (actual)

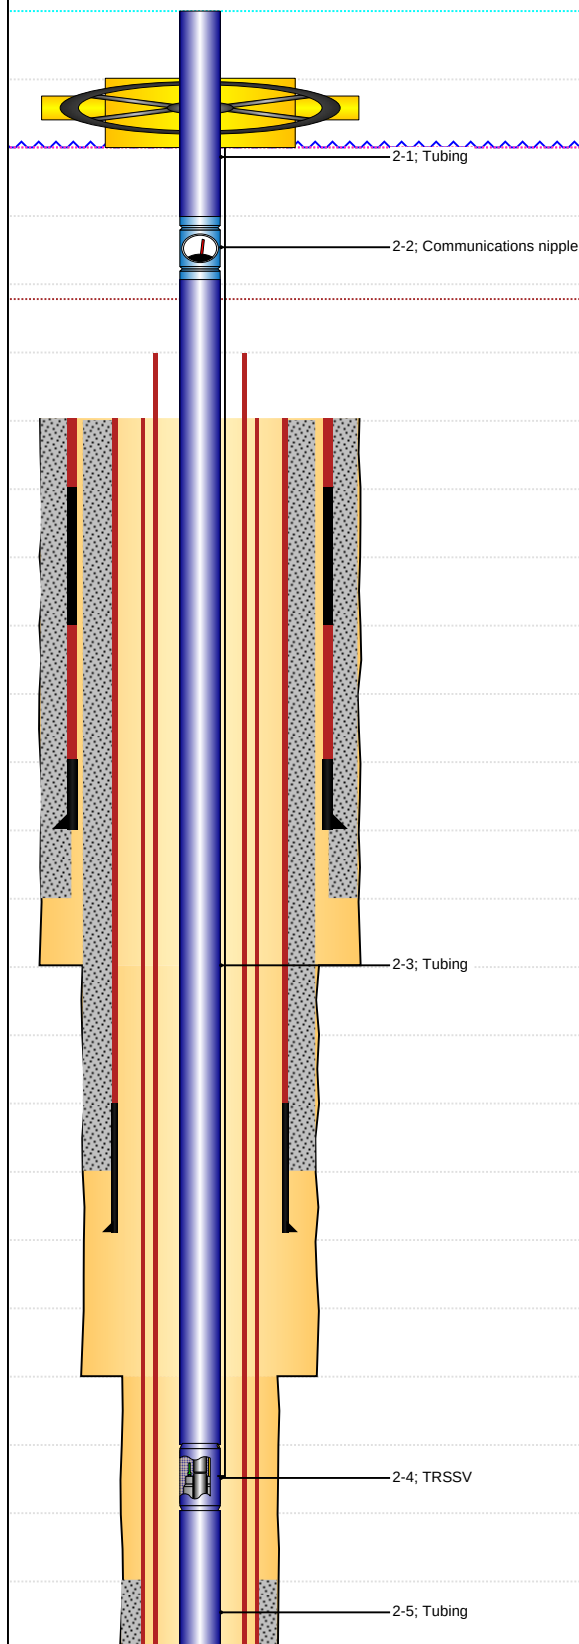

API/UWI 0987656789		Operator Peloton Oil & Gas					
Original KB Elevation (ft) 210.00		KB-Ground Distance (ft)	Spud Date 2000-02-21	Rig Release Date 2000-03-18			
Surface Legal Location			Latitude (°) 51° 0' 0" N	Longitude (°) 114° 0' 0" W			
Original Hole							
Wellbore API/UWI 52994921		Btm. Loc.	Profile Type Directional	KO MD (ftKB) 1,381.2	VS Dir (°)		
Proposed Deviation Survey			Actual Deviation Survey Main Hole Survey, Proposed? No				
Size (in)		Act Top (ftKB)		Act Btm (ftKB)			
36		1,381.2		1,610.9			
26		1,610.9		2,257.2			
17 1/2		2,257.2		4,281.5			
12 1/4		4,281.5		12,503.3			
Plug Back Total Depths							
Date	Depth (ftKB)	Method	Com				
2000-05-15	12,330.1						
2000-05-20	12,089.9						
Formations							
Formation Name	Geologic Age	Element Type	H2S Conc (%)	Final Top MD (ftKB)	Final Top TVD (ftKB)		
Blue Ridge				2,200.0	2,199.4		
Ten Oaks				4,260.0	4,061.2		
Haverty Limestone				6,942.3	5,828.9		
Green River				8,907.5	7,157.5		
Upper Deer Park				12,089.9	9,278.7		
Lower Deer Park				12,253.9	9,384.5		
TD							
Deviation Surveys							
Date	Des		Prop?	Definitive?			
2000-03-16	Main Hole Survey		No	No			
Reservoirs							
Res Name		Top (ftKB)	Btm (ftKB)	Res Datum Depth (ft)			
Structural Casing, 1,598.8ftKB							
Run Date 2000-02-22	Centralizers 2/joint every 4th joint		Scratchers None		Drift Mi... 28.000		
OD (in)	Item Des	Btm (ftKB)	Jts	ID (in)	Wt (kips)	Grade	Top Thread
30	Casing Joint(s)	1,483.6	2	28.000	31.7	X-52	RL-4HT
30	Cross-Over Joint	1,521.6	1	28.000	11.8	X-52	RL-4HT
30	Casing Joint(s)	1,559.9	1	28.000	11.9	X-52	RL-4S
30	Float Shoe Joint	1,598.8	1	28.000	12.0	X-52	RL-4S
Conductor Pipe, 2,239.0ftKB							
Run Date 2000-02-23	Centralizers Two every 5th joint		Scratchers None		Drift Mi... 17.500		
OD (in)	Item Des	Btm (ftKB)	Jts	ID (in)	Wt (kips)	Grade	Top Thread
20	Casing Joint(s)	2,199.8	21	18.750	105.9	X-56	RL-4S
20	Float Shoe	2,239.0	1	18.750	5.1	X-56	RL-4S
Surface Casing, 4,253.0ftKB							
Run Date 2000-03-01	Centralizers 2/joint on shoe track.		Scratchers None		Drift Mi... 12.410		
OD (in)	Item Des	Btm (ftKB)	Jts	ID (in)	Wt (kips)	Grade	Top Thread
13 3/8	Casing Joint(s)	4,172.6	72	12.415	189.8	K-55	BTC
13 3/8	Float Collar	4,173.8	1	12.415	0.1	K-55	BTC
13 3/8	Casing Joint(s)	4,251.2	2	12.415	5.3	K-55	BTC
13 3/8	Float Shoe	4,253.0	1	12.415	0.1	K-55	BTC
Production Casing, 12,478.9ftKB							
Run Date 2000-03-17	Centralizers 2/joint on shoe track		Scratchers		Drift Mi... 8.525		
OD (in)	Item Des	Btm (ftKB)	Jts	ID (in)	Wt (kips)	Grade	Top Thread
10.752	Casing Joint(s)	3,817.5	62	9.602	135.4	L-80	VAM
10.752	Cross Over	3,819.0	1	8.524	0.1	L-80	VAM
9 5/8	Casing Joint(s)	12,398.6	222	8.524	459.0	L-80	LTC
9 5/8	Float Collar	12,399.7	1	8.524	0.1	L-80	LTC
9 5/8	Casing Joint(s)	12,477.3	2	8.524	4.1	L-80	LTC
9 5/8	Float Shoe	12,478.9	1	8.524	0.1	L-80	LTC
Structural Cement, Casing, 2000-02-22 11:15							
Cementing Company Halliburton		Evaluation Method Returns to Surface		Cement Evaluation Results Pumped 100% excess to ensure good cement to ML			
Stg # 1	Description Casing Cement			Top (ftKB) 1,381.2	Btm (ftKB) 1,604.3	Full Return? Yes	
Fluid	Class	Amount (sacks)	Yield (ft³/sack)	Mix H2O Ratio (gal/sack)	Vol Pumped (bbl)	Fluid Des	
Lead Cement	G	23	53.52	234.05	222.0	Neat	
Conductor Cement, Casing, 2000-02-23 21:30							
Cementing Company Halliburton		Evaluation Method Returns to Surface		Cement Evaluation Results Confirmed returns to wellhead			
Stg # 1	Description Casing Cement			Top (ftKB) 1,381.2	Btm (ftKB) 2,237.5	Full Return? Yes	

Complete Well Summary Sample 11 - Full Data


Deviated - Original Hole, 2009-09-15 10:35:30 AM
Vertical schematic (actual)

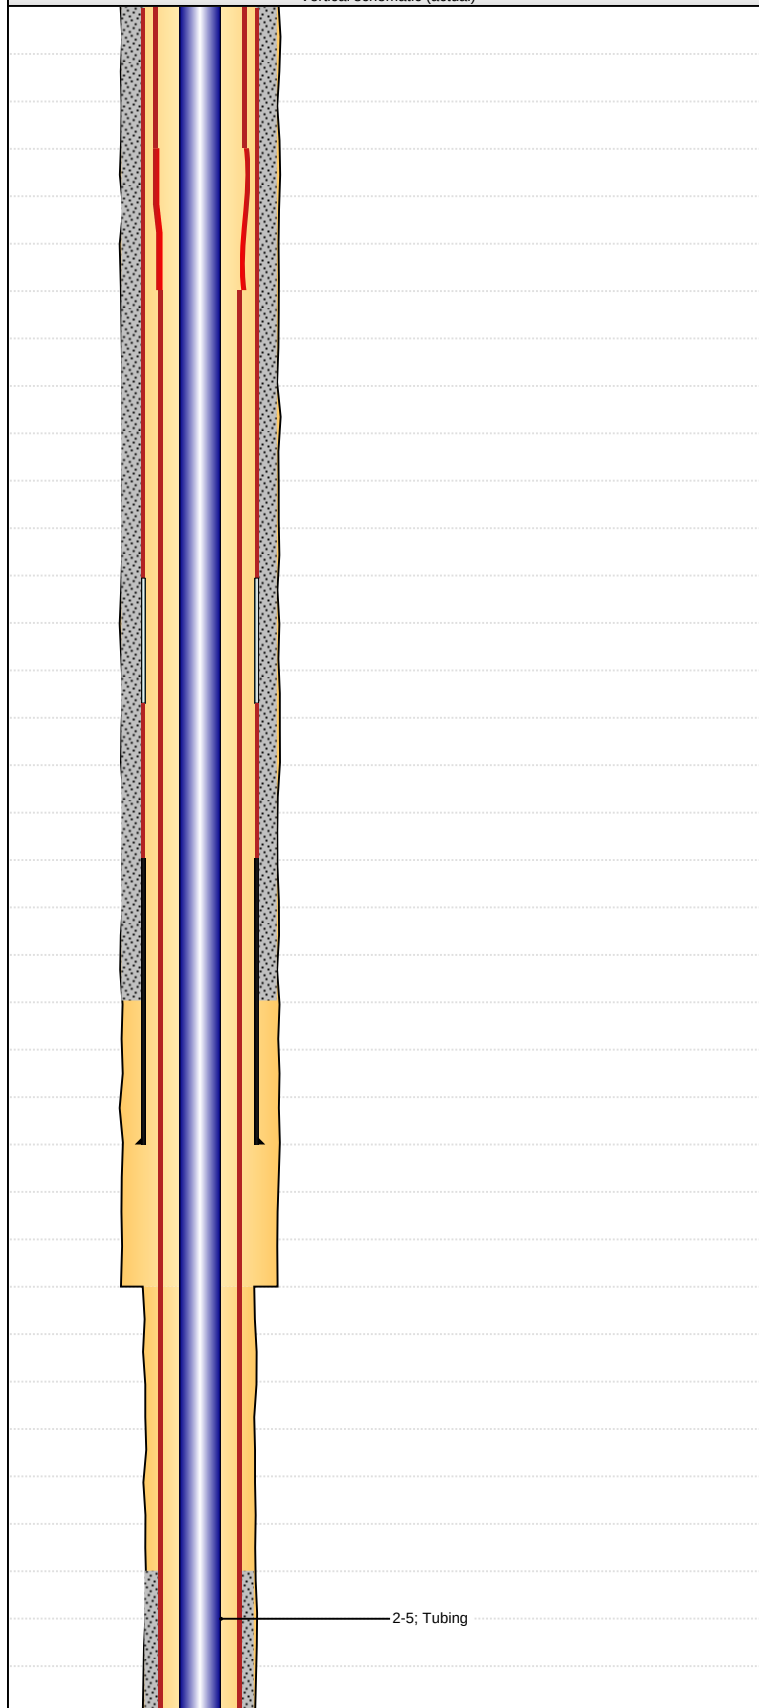

Fluid	Class	Amount (sacks)	Yield (ft³/sack)	Mix H2O Ratio (gal/sack)	Vol Pumped (bbl)	Fluid Des		
Lead	G	3	568.80	100.24	157.0	LIQUID ADDITIVE EXT.		
Tail	G	7	226.80	52.62	295.0	Neat		
Surface Casing Cement, Casing, 2000-03-01 18:45								
Cementing Company Halliburton			Evaluation Method Temperature Log		Cement Evaluation Results Ran temp log to confirm TOC			
Stg #	Description				Top (ftKB)	Btm (ftKB)	Full Return?	
1	Casing Cement				2,775.6	4,252.0	Yes	
Fluid	Class	Amount (sacks)	Yield (ft³/sack)	Mix H2O Ratio (gal/sack)	Vol Pumped (bbl)	Fluid Des		
Tail	G	21	52.62	283.50	196.0	Neat		
Production Casing Cement, Casing, 2000-03-18 01:30								
Cementing Company Halliburton			Evaluation Method Temperature Log		Cement Evaluation Results Temp log confirmed success and TOC			
Stg #	Description				Top (ftKB)	Btm (ftKB)	Full Return?	
1	Casing Cement				4,899.0	12,503.0	Yes	
Fluid	Class	Amount (sacks)	Yield (ft³/sack)	Mix H2O Ratio (gal/sack)	Vol Pumped (bbl)	Fluid Des		
Lead Cement	G	2	257.19	292.57	75.0	Including gel and retarder		
Tail Cement	G	7	283.50	362.87	335.0	Neat with Retarder		
Other In Hole								
OD (in)	Des			Top (ftKB)	Btm (ftKB)	ID (in)	Make	Model
7	Bridge Plug - Permanent			12,330.0	12,334.0		Halliburton	EZ Drill
SSMC, Cameron on 2000-02-22 00:00								
Install Date	Type		Make		WP (psi)	Size (in)	Last Overhaul...	
2000-02-22	SSMC		Cameron		10,000.0	18.750		
Wellhead Components								
Make	Model	Section	Top Conn Typ	Top Sz (in)	Btm Conn Typ	Btm Sz (in)	Des	WP (psi)
Cameron	SSMC	A	Snapping Lockdown	30.000	Welded	30.000	30" Conductor Landing Ring	10,000.0
Cameron	SSMC	B	Snapping Lockdown	20.750	Snapping Lockdown	20.750	20-3/4" Casing Head	10,000.0
Cameron	SSMC	C	Snapping Lockdown	20.750	Snapping Lockdown	20.750	13-5/8" Casing Head	10,000.0
Cameron	SSMC	C	Snapping Lockdown	13.625	Snapping Lockdown	13.625	12-1/4" Casing Head	10,000.0
Cameron	SSMC	D	Snapping Lockdown	13.625	Snapping Lockdown	20.750	Flange Lock Connector	10,000.0
General Notes								
Date	Com							
Drilling - original, 2000-02-21 00:00								
Job Category		Primary Job Type				Start Date		End Date
Drilling		Drilling - original				2000-02-21		2001-03-18
Drilling - original, 2000-02-21 00:00								
AFE Number		AFE+Supp Amt (Cost)		Total Fld Est (Cost)		Total Final Invoice (Cost)		
9876543		10,343,000.00		10,127,291.47		10,217,000.00		
Summary								
No major problems were encountered while drilling this well. Note that the well was completed under budget and within the allocated number of days.								
Poss Cost Save (Cost)		Poss Time Save (hr)		Est Prob Cost (Cost)		Est Lost Time (hr)		
625.00		8.00		38,500.00		11.50		
Phases								
Phase Type 1					Planned Likely Phase Cost (Cost)	Pl Cum Days ML (days)	Planned End Depth (ftKB)	
Surface					800,000.00	2.00	2,260.0	
Surface					1,125,000.00	4.00	2,260.0	
Intermediate					2,250,000.00	9.00	4,300.0	
Intermediate					6,500,000.00	11.00	4,300.0	
Production					7,000,000.00	25.00	12,750.0	
Production					500,000.00	26.50	12,750.0	
Production					8,500,000.00	29.50	12,750.0	
Job Contacts								
Contact Name	Company			Title	Office	Mobile		
Bill Parcels	Geoservices			Manager	555-441-3001	555-133-0478		
Jr. Seau	West Houston			Asst. Manager	555-332-3341	555-332-7752		
Michael Strahan	Dowell			Cementer	555-325-9939	555-325-7734		
Terry Glenn	Nabors			Rig Supervisor	555-380-3991	555-300-3991		
David Lee Roth	Rocks R Us			Sr Geologist	555-111-2345			
Judy Garland	Hydrosearch QC			Customer Service	555-993-4995	555-993-0533		
Tom Brady	Camco			Salesman	555-494-3881	555-494-8578		
Glen Ford	Halliburton			Operations Manager	555-329-9393	555-329-2442		
Michael Anthony	Peloton			Engineer	555-133-4456	555-133-9427		
Eddie Van Halen	Peloton			Consultant	555-200-3989	555-029-9115		
Cliff Montgomery	Security ERA			Regional Manager	555-494-4985	555-494-7882		
Sammy Hagar	Schlumberger			Engineer	555-992-0021	555-992-3226		
Randy Moss	GeoDiamond			Sales Assistant	555-994-2343	555-994-8352		

Complete Well Summary Sample 11 - Full Data

Deviated - Original Hole, 2009-09-15 10:35:30 AM
Vertical schematic (actual)

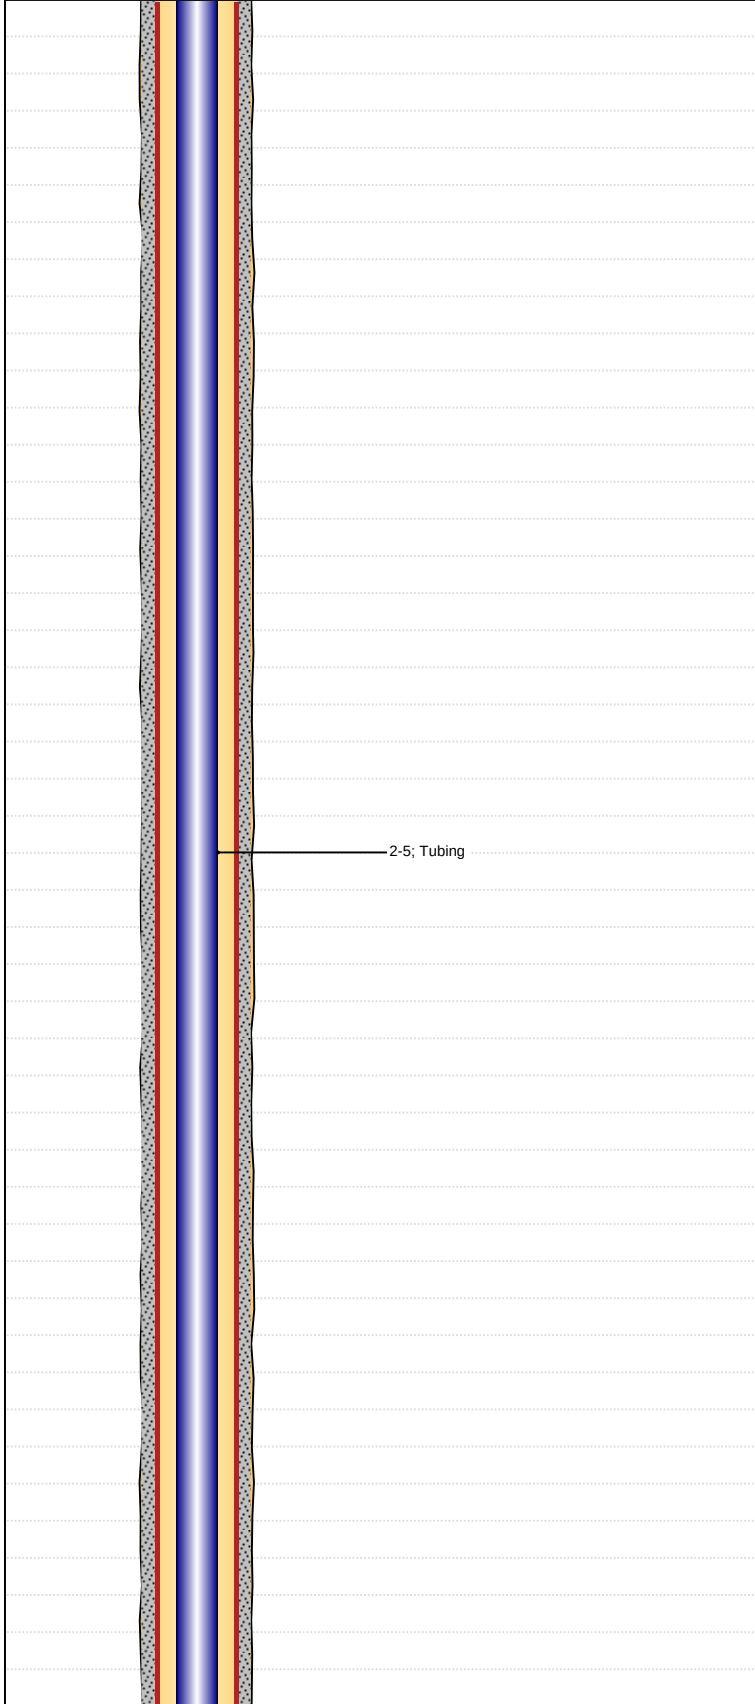


BHA #1, 36" Drilling Assy						
BHA #	1	Size (in)	26	Model	S3SJ	IADC Codes
Depth In (ftKB)	1,381.2	Depth Out (ftKB)	1,610.9	Drilled (ft)	229.66	Drill Time (hr)
Bit Hrs Out...	11.52	IADC Bit Dull	1-1-NO-A-1-0-NO-TD	Bit Hrs Out...	11.52	IADC Bit Dull
String Components						
Hughes S3SJ, 36" Hole Opener, 36" Hole Opener, Float Sub, Drill Collar, 36" Integral Blade Stabilizer, Drill Collar, Non-Mag Drill Collar, Cross Over, Drill Collar, Drilling Jar, Drill Collar, Cross Over, Heavy Weight Drill Pipe, Drill Pipe						
BHA #2, 26" Drilling Assy						
BHA #	2	Size (in)	26	Model	S3SJ	IADC Codes
Depth In (ftKB)	1,610.9	Depth Out (ftKB)	2,257.0	Drilled (ft)	646.11	Drill Time (hr)
Bit Hrs Out...	4.00	IADC Bit Dull	1-1-NO-A-2-0-NO-TD	Bit Hrs Out...	4.00	IADC Bit Dull
String Components						
Security S3SJ, Float Sub, Drill Collar, Integral Blade Stabilizer, Drill Collar, Cross Over, Non-Mag Drill Collar, Drill Collar, Drilling Jar, Drill Collar, Cross Over, Heavy Weight Drill Pipe, Drill Pipe						
BHA #3, 17-1/2" Directional Assy						
BHA #	3	Size (in)	17 1/2	Model	SS33SGJ4	IADC Codes
Depth In (ftKB)	2,257.0	Depth Out (ftKB)	4,281.5	Drilled (ft)	2,024.50	Drill Time (hr)
Bit Hrs Out...	29.00	IADC Bit Dull	2-2-WT-A-E-0-FC-TD	Bit Hrs Out...	29.00	IADC Bit Dull
String Components						
Security SS33SGJ4, Bent Housing, Cross Over, Float Sub, Non-Mag Pony Collar, Non-Mag Pony Collar, Cross Over, MWD Tool, Cross Over, Non-Mag Integral Blade Stabilizer RM3 -, Non-Mag Drill Collar, Drill Collar, Cross Over, Heavy Weight Drill Pipe, Drilling Jar, Heavy Weight Drill Pipe, Drill Pipe						
BHA #4, 12-1/4" Directional Assy						
BHA #	4	Size (in)	17 1/2	Model	SS33SGJ4	IADC Codes
Depth In (ftKB)	4,281.5	Depth Out (ftKB)	7,000.0	Drilled (ft)	2,718.50	Drill Time (hr)
Bit Hrs Out...	53.25	IADC Bit Dull	1-1-NO-A-D-1-NO-HP	Bit Hrs Out...	53.25	IADC Bit Dull
String Components						
Security SS33SGJ4, Pony Collar, Variable Gauge Stabilizer, 11.5-12.25", Non-Mag Pony Collar, Cross Over, MWD Tool, Cross Over, Non-Mag Integral Blade Stabilizer RM3 -, Non-Mag Drill Collar, Cross Over, Heavy Weight Drill Pipe, Drilling Jar, Heavy Weight Drill Pipe, Drill Pipe						
BHA #5, 12-1/4" Coring Assembly						
BHA #	5	Size (in)	12 1/4	Model	CSP 107	IADC Codes
Depth In (ftKB)	7,000.0	Depth Out (ftKB)	7,060.0	Drilled (ft)	60.00	Drill Time (hr)
Bit Hrs Out...	3.00	IADC Bit Dull	1-1-NO-C-X-1-NO-BHA	Bit Hrs Out...	3.00	IADC Bit Dull
String Components						
Security DBS CSP 107, Core Barrel, Core Barrel Extension, Cross Over, Heavy Weight Drill Pipe, Drilling Jar, Heavy Weight Drill Pipe, Drill Pipe						
BHA #6, 12-1/4" Directional Assy						
BHA #	6	Size (in)	17 1/2	Model	SS33SGJ4	IADC Codes
Depth In (ftKB)	7,060.0	Depth Out (ftKB)	8,960.0	Drilled (ft)	1,899.97	Drill Time (hr)
Bit Hrs Out...	73.50	IADC Bit Dull	1-1-NO-A-D-1-NO-HP	Bit Hrs Out...	73.50	IADC Bit Dull
String Components						
Security SS33SGJ4, Pony Collar, Variable Gauge Stabilizer, 11.5-12.25", Non-Mag Pony Collar, Cross Over, MWD Tool, Cross Over, Non-Mag Integral Blade Stabilizer RM3 -, Non-Mag Drill Collar, Cross Over, Heavy Weight Drill Pipe, Drilling Jar, Heavy Weight Drill Pipe, Drill Pipe						
BHA #7, 12-1/4" Directional Assy						
BHA #	7	Size (in)	12 1/4	Model	M42X	IADC Codes
Depth In (ftKB)	8,960.0	Depth Out (ftKB)	12,208.0	Drilled (ft)	3,248.03	Drill Time (hr)
Bit Hrs Out...	59.25	IADC Bit Dull	3-3-WT-A-D-0-NO-PR	Bit Hrs Out...	59.25	IADC Bit Dull
String Components						
GeoDiamond M42X, Non-Mag Pony Collar, Variable Gauge Stabilizer, 11.5-12.25", Non-Mag Pony Collar, Cross Over, MWD Tool, Cross Over, Non-Mag Integral Blade Stabilizer RM3 -, Non-Mag Drill Collar, Cross Over, Heavy Weight Drill Pipe, Drilling Jar, Heavy Weight Drill Pipe, Drill Pipe						
BHA #8, 12-1/4" Directional Assy						
BHA #	8	Size (in)	12 1/4	Model	M42X	IADC Codes
Depth In (ftKB)	12,208.0	Depth Out (ftKB)	12,349.1	Drilled (ft)	141.08	Drill Time (hr)
Bit Hrs Out...	19.25	IADC Bit Dull	3-3-WT-A-3-0-BT-LOG	Bit Hrs Out...	19.25	IADC Bit Dull
String Components						
GeoDiamond M42X, Non-Mag Pony Collar, Underguage Integral Blade Stabilizer, Non-Mag Pony Collar, Cross Over, MWD Tool, Cross Over, Non-Mag Integral Blade Stabilizer RM3 -, Non-Mag Drill Collar, Cross Over, Heavy Weight Drill Pipe, Drilling Jar, Heavy Weight Drill Pipe, Drill Pipe						
BHA #9, 12-1/4" Directional Assy						
BHA #	9	Size (in)	12 1/4	Model	M42X	IADC Codes
Depth In (ftKB)	12,349.1	Depth Out (ftKB)	12,385.2	Drilled (ft)	36.09	Drill Time (hr)
Bit Hrs Out...	28.75	IADC Bit Dull	3-4-WT-S-D-0-NO-PR	Bit Hrs Out...	28.75	IADC Bit Dull
String Components						
GeoDiamond M42X, Non-Mag Pony Collar, Underguage Integral Blade Stabilizer, Non-Mag Pony Collar, Cross Over, MWD Tool, Cross Over, Non-Mag Integral Blade Stabilizer RM3 -, Non-Mag Drill Collar, Cross Over, Heavy Weight Drill Pipe, Drilling Jar, Heavy Weight Drill Pipe, Drill Pipe						

Complete Well Summary Sample 11 - Full Data

Deviated - Original Hole, 2009-09-15 10:35:31 AM

Vertical schematic (actual)

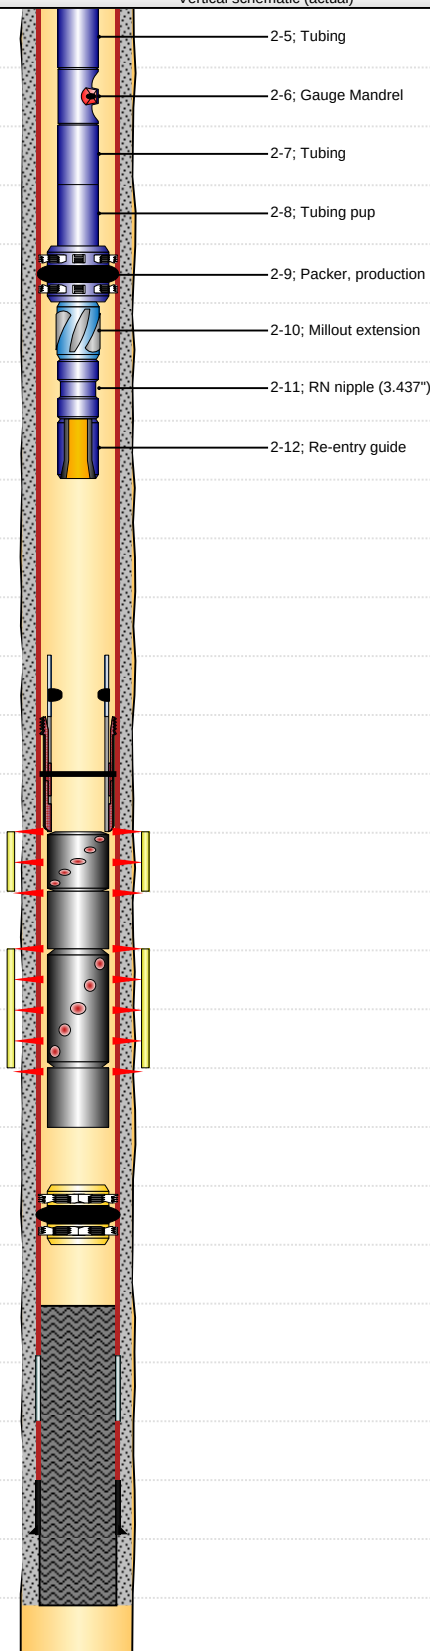

BHA #10, 12-1/4" Directional Assy											
BHA #	10	Size (in)	12 1/4	Model	SS33SGJ4	IADC Codes	115	IADC Bit Dull	2-6-PB-H-2-8-WT-PR		
Depth In (ftKB)	12,385.2	Depth Out (ftKB)	12,503.3	Drilled (ft)	118.11	Drill Time (hr)	12.25	Bit Hrs Out...	12.25	IADC Bit Dull	2-6-PB-H-2-8-WT-PR
String Components											
Security SS33SGJ4, Non-Mag Pony Collar, Undergauge Integral Blade Stabilizer, Non-Mag Pony Collar, Cross Over, MWD Tool, Cross Over, Non-Mag Integral Blade Stabilizer RM3 -, Non-Mag Drill Collar, Cross Over, Heavy Weight Drill Pipe, Drilling Jar, Heavy Weight Drill Pipe, Drill Pipe											
Completion, 2000-05-16 00:00											
Job Category		Primary Job Type				Start Date		End Date			
Completion/Workover		Completion				2000-05-16		2000-06-03			
Completion, 2000-05-16 00:00											
AFE Number		AFE+Supp Amt (Cost)		Total Fid Est (Cost)		Total Final Invoice (Cost)					
1234567C		7,753,000.00		7,672,928.47							
Summary											
Poss Cost Save (Cost)		Poss Time Save (hr)		Est Prob Cost (Cost)		Est Lost Time (hr)					
Phases											
Phase Type 1						Planned Likely Phase Cost (Cost)	Pl Cum Days ML (days)	Planned End Depth (ftKB)			
Job Contacts											
Contact Name		Company		Title		Office		Mobile			
Terry Glenn		Nabors		Rig Supervisor		555-380-3991		555-300-3991			
Michael Strahan		Dowell		Cementer		555-325-9939		555-325-7734			
Tom Brady		Camco		Salesman		555-494-3881		555-494-8578			
Bill Parcels		Geoservices		Manager		555-441-3001		555-133-0478			
Randy Moss		GeoDiamond		Sales Assistant		555-994-2343		555-994-8352			
Glen Ford		Halliburton		Operations Manager		555-329-9393		555-329-2442			
Jr. Seau		West Houston		Asst. Manager		555-332-3341		555-332-7752			
Eddie Van Halen		Peloton		Consultant		555-200-3989		555-029-9115			
Sammy Hagar		Schlumberger		Engineer		555-992-0021		555-992-3226			
Michael Anthony		Peloton		Engineer		555-133-4456		555-133-9427			
Judy Garland		Hydrosearch QC		Customer Service		555-993-4995		555-993-0533			
Cliff Montgomery		Security ERA		Regional Manager		555-494-4985		555-494-7882			
BHA #<stringno>, <des>											
BHA #	Size (in)	Model		IADC Codes		IADC Bit Dull					
Depth In (ftKB)		Depth Out (ftKB)		Drilled (ft)		Drill Time (hr)	Bit Hrs Out...	IADC Bit Dull			
String Components											
Logs											
Date	Type			Top (ftKB)	Btm (ftKB)	Logging Company					
2000-03-12	GR - LDT - CNR - DIT			6,233.6	7,466.1	Schlumberger Wireline & Testing					
2000-03-12	GR-DSI			3,937.0	12,503.3	Schlumberger Wireline & Testing					
2000-05-19	GR - CCL - Resistivity			10,000.0	12,500.0	Schlumberger Wireline & Testing					
Bottom Hole Cores											
Core #	Type		Top (ftKB)	Btm (ftKB)	Recov (ft)	Wellbore					
	Conventional		12,247.4	12,322.8	60.0	Original Hole					
Leak Off and Formation Integrity Tests											
Test Date	Last Casing String Run			P Surf Applied (psi)	Depth (ftKB)	Dens Fluid (lb/gal)	Leak off?				
2000-02-28	Conductor Pipe, 2,239.0ftKB				2,237.0	9.20	No				
2000-03-03	Surface Casing, 4,253.0ftKB			700.0	4,285.0	10.50	Yes				
Schematic Annotations											
Depth (ftKB)				Annotation							
1,500.0				Casing set 12' off bottom							
Production Failures											
Failure Date	Failure Des	Fail Typ	Cause	Failed Item		Resolved Date	Est Fail (Cost)				
