
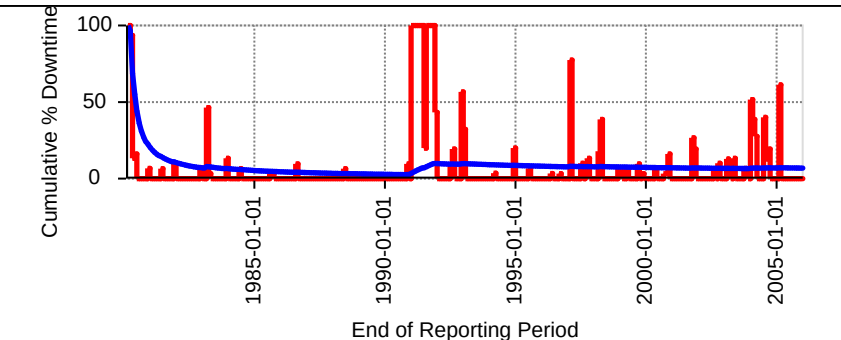
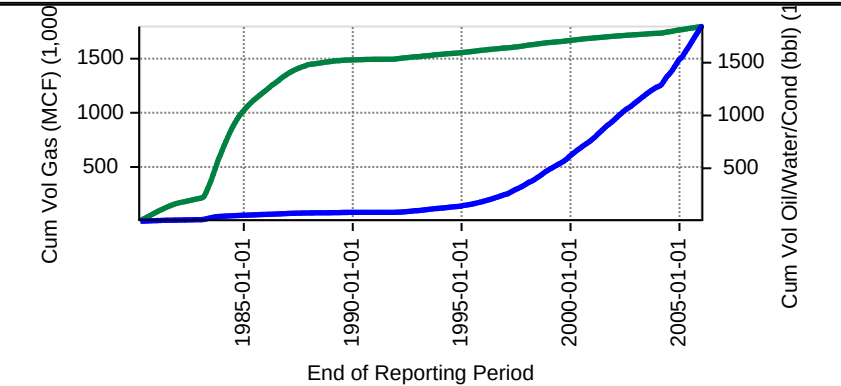


Well Name: Sample 37 - ESP

API/UWI 1234567890	Surface Legal Location	License # 1234	Well Configuration Type Vertical	Ground Elevation (ft) 2,522.97	Casing Flange Elevation (ft) 2,532.81	KB-Ground Distance (ft) 19.03	KB-Casing Flange Distance (ft) 9.19
-----------------------	------------------------	-------------------	-------------------------------------	-----------------------------------	--	----------------------------------	--

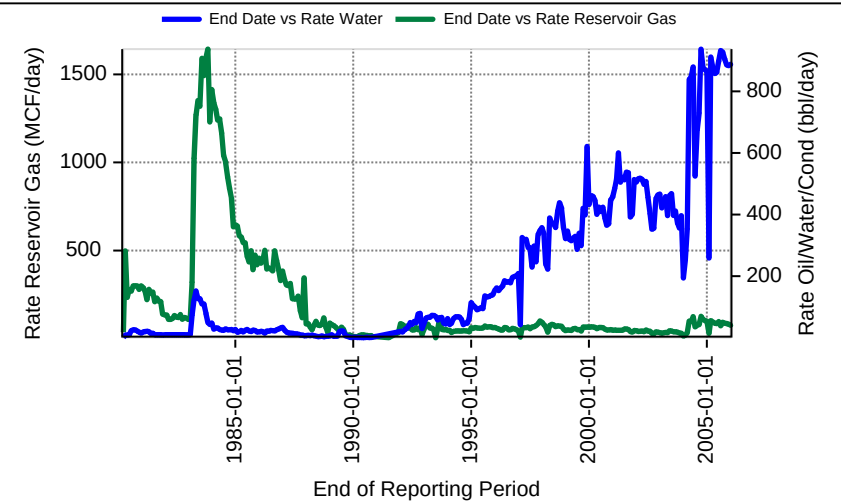

Summarized Production Data (Most Recent at Top)										
Start Date	End Date	Prod Time (days)	DownTm (days)	Vol ResGas (MCF)	Vol Oil (bbl)	Vol Water (bbl)	Q Reservoir Gas (MCF/day)	Q Oil (bbl/day)	Q Water (bbl/day)	Water Gas Ratio (%)
2005-12-01	2006-01-01	31.00	0.00	2,367.000	4085.000	27528.002	76.35	131.77	888.00	6.5
2005-11-01	2005-12-01	30.00	0.00	2,489.000	3798.000	26524.000	82.97	126.60	884.13	6.0
2005-10-01	2005-11-01	31.00	0.00	2,677.000	4247.000	27479.001	86.35	137.00	886.42	5.8
2005-09-01	2005-10-01	30.00	0.00	2,629.000	4277.000	27190.001	87.63	142.57	906.33	5.8
2005-08-01	2005-09-01	31.00	0.00	2,892.000	4322.000	28767.002	93.29	139.42	927.97	5.6
2005-07-01	2005-08-01	31.00	0.00	2,274.000	4281.000	28918.001	73.35	138.10	932.84	7.1
2005-06-01	2005-07-01	30.00	0.00	2,920.000	4223.000	26910.000	97.33	140.77	897.00	5.2
2005-05-01	2005-06-01	31.00	0.00	2,653.000	4431.000	26723.001	85.58	142.94	862.03	5.7
2005-04-01	2005-05-01	30.00	0.00	2,624.000	4203.000	25748.001	87.47	140.10	858.27	5.5
2005-03-01	2005-04-01	31.00	0.00	2,949.000	4681.000	27173.002	95.13	151.00	876.55	5.2
2005-02-01	2005-03-01	28.00	0.00	2,870.000	4150.000	25532.000	102.50	148.21	911.86	5.0
2005-01-01	2005-02-01	12.00	19.00	939.000	1430.000	8033.000	30.29	46.13	259.13	4.8
2004-12-01	2005-01-01	31.00	0.00	3,088.000	4901.000	26814.001	99.61	158.10	864.97	4.9
2004-11-01	2004-12-01	30.00	0.00	3,082.000	4698.000	26122.002	102.73	156.60	870.73	4.8
2004-10-01	2004-11-01	31.00	0.00	3,407.000	5250.000	27160.002	109.90	169.35	876.13	4.5
2004-09-01	2004-10-01	30.00	0.00	3,818.000	5703.000	28119.001	127.27	190.10	937.30	4.1
2004-08-01	2004-09-01	25.00	6.00	2,473.000	4201.000	22574.000	79.77	135.52	728.19	5.1
2004-07-01	2004-08-01	27.00	4.00	2,388.000	3930.000	20851.001	77.03	126.77	672.61	4.9
2004-06-01	2004-07-01	18.00	12.00	2,018.000	2787.000	15756.001	67.27	92.90	525.20	4.4

Completion/Workover Job History			
Job Type	Start Date	End Date	Summary
Initial Completion	1980-04-12	1980-04-15	
Casing Repair	1983-02-11	1997-07-10	
Pump Repair	2002-09-26	2002-09-28	
Pump Repair	2003-09-16	2003-09-18	
Pump Repair	2003-10-21	2003-10-23	Replaced parted rod, replaced pump & 31 worn rod boxes
Casing Repair	2003-12-16	2004-01-13	
Reconfigure Tubing/Components	2004-02-16	2004-02-26	
Pump Repair	2004-06-17	2004-07-07	Replaced 2 motors, seal assemblies, & cable @ top. Tested. Ran new pumps, motors & seal assemblies.
Pump Repair	2004-07-22	2004-07-23	Standing valve ran in, tubing okay.
Pump Repair	2004-08-11	2004-08-18	Tested all ESP equipment, found bad seal between pumps, re-ran pumps, motors, & new seal assembly.
Pump Repair	2005-01-10	2005-01-12	
