


Well Name: Sample 11 - Full Data

Surface Casing

API/UWI 0987656789	Surface Legal Location	Field Name Akuinu	License # 8818838	State/Province Texas	Well Configuration Type Deviated
Ground Elevation (ft)	Casing Flange Elevation (ft) 0.00	KB-Ground Distance (ft)	KB-Casing Flange Distance (ft) 210.00	Spud Date 2000-02-21 00:00	Rig Release Date 2000-03-18 00:00

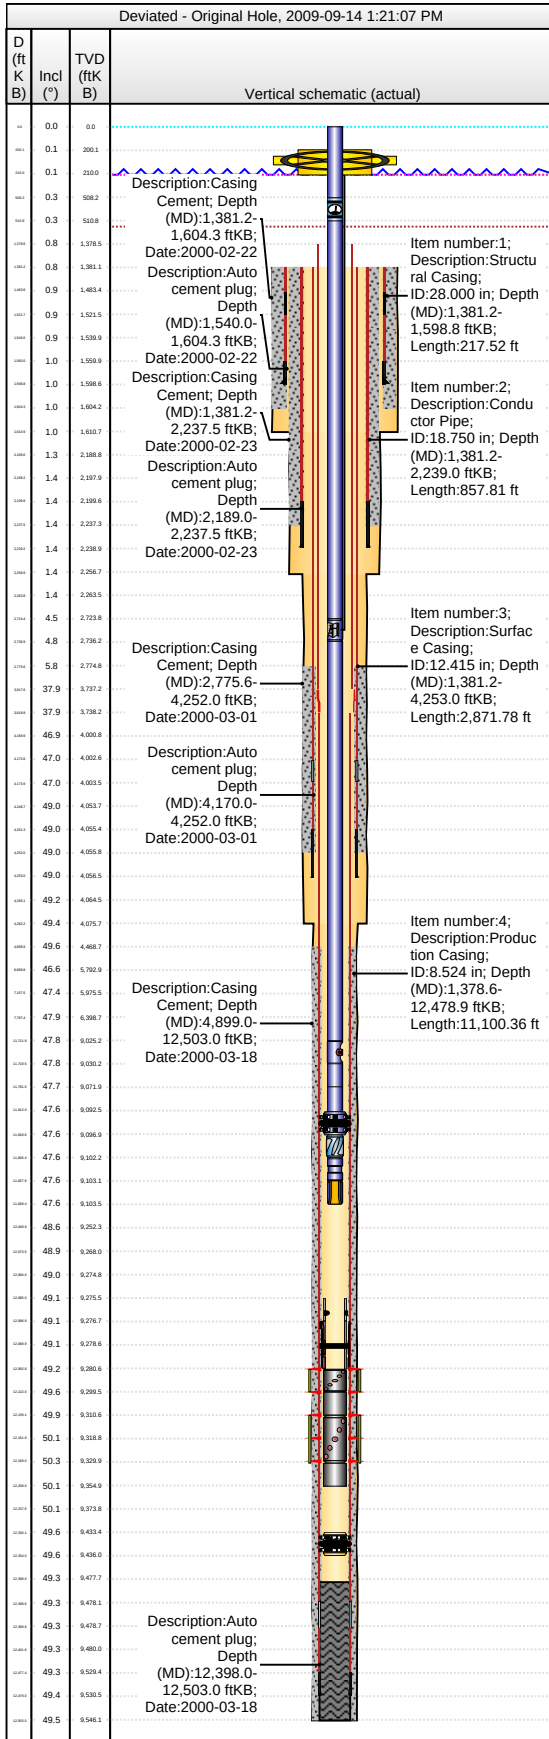

Wellbore			
Wellbore Name Original Hole	Profile Type Directional	Kick Off Depth (ftKB) 1,381.2	Vertical Section Direction (°)
Section Des	Size (in)	Act Top (ftKB)	Act Btm (ftKB)
	36	1,381.2	1,610.9
	26	1,610.9	2,257.2
	17 1/2	2,257.2	4,281.5
	12 1/4	4,281.5	12,503.3

Wellhead				
Type SSMC				
Des	Make	Model	SN	WP Top (psi)
20-3/4" Casing Head	Cameron	SSMC	92355-233	10,000.0
13-5/8" Casing Head	Cameron	SSMC	33455-352	10,000.0
12-1/4" Casing Head	Cameron	SSMC	33455-352	10,000.0

Last Mud Check							
Date	Type	Depth (ftKB)	Dens (lb/gal)	Vis (s/qt)	Gel (10s) (lb/100ft²)	Gel (10m) (lb/100ft²)	YP OR (lb/100ft²)

Casing								
Casing Description Surface Casing				Run Date 2000-03-01 07:15		Set Depth (ftKB) 4,253.0		Wellbore Original Hole
Centralizers 2/joint on shoe track.				Scratchers None				
Jts	Item Des	OD (in)	ID (in)	Wt (lb/ft)	Grade	Len (ft)	Top (ftKB)	Btm (ftKB)
72	Casing Joint(s)	13 3/8	12.415	68.00	K-55	2,791.40	1,381.2	4,172.6
1	Float Collar	13 3/8	12.415	68.00	K-55	1.15	4,172.6	4,173.8
2	Casing Joint(s)	13 3/8	12.415	68.00	K-55	77.49	4,173.8	4,251.2
1	Float Shoe	13 3/8	12.415	68.00	K-55	1.74	4,251.2	4,253.0

Cement: Surface Casing Cement		
Cementing Start Date 2000-03-01	Cementing End Date 2000-03-01	Wellbore Original Hole
Evaluation Method Temperature Log	Cement Evaluation Results Ran temp log to confirm TOC	
Comment Job was successful		

Cement Stage: Surface Casing Cement					
Top Depth (ftKB) 2,775.6	Bottom Depth (ftKB) 4,252.0	Full Return? Yes	Vol Ceme... 0.0	Top Plug? Yes	Bottom Plug? Yes
Q Pump Init (bbl/min) 103	Q Pump Final (bbl/min) 3	Avg Pump Rate (bbl/min) 10	Final Pump Pressure (psi) 350.0	Plug Bump Pressure (psi) 1,500.0	
Pipe Reciprocated? Yes	Stroke (ft) 35.00	Reciprocation Rate (spm) 3	Pipe Rotated? Yes	Pipe RPM (rpm) 18	
Tagged Depth (ftKB) 4,170.0	Tag Method Drill Bit	Depth Plug Drilled Out... 4,282.0	Drill Out Diameter (in) 12 1/4	Drill Out Date 2000-03-03	

Cement Fluid: Surface Casing Cement					
Fluid Type Tail	Fluid Description Neat	Amount (s...) 21	Class G	Volume Pumped (bbl) 196.0	
Estimated Top (ftKB) 2,775.6	Est Btm (ftKB) 4,252.0	Yield (ft³/sack) 52.62	Mix H2O Ratio (gal/sack) 283.50	Free Water (%) 4.00	
Density (lb/gal) 15.80	Plastic Viscosity (cp) 36.0	Thickening Time (hr) 2.60	1st Compressive Strength (psi) 1,880.0		

Cement Fluid Additives		
Add	Type	Conc
Kwik Seal	Lost Circulation Additive	
